LOWER KING STREET STREETSCAPE NOTICE

Call Su - 720-3886 July 10, 2008 Call Bret - 860-3696

For website information on Streetscape, please click on: http://www.charlestoncity.info/dept/content.aspx?nid=391 or http://www.charlestoncity.info/dept/content.aspx?nid=391 or


- Electrical ductbank work could begin late next week at the intersection of King and Market Streets proceeding down the west side of King Street. Parking meters will be bagged, and there will be one lane of traffic open in that area. Signage will be placed near King and Beaufain Streets to alert drivers to the traffic control plan.
- Good progress is being made at <u>Horlbeck Alley</u> as electrical conduit and the new water main is being installed. Streetscape staff will contact merchants who park in the private lots in those areas when different parking arrangements are necessary. Signage for this project is in place along King, Broad and Meeting Streets.
- The sewer line repair at <u>155 King Street</u> near Jacob's Alley will be completed this week and the point repair between <u>151 & 153 King Street</u> will be completed early next week.
- Also next week, sewer point repairs will potentially occur at the <u>Horlbeck</u> Alley intersection, just <u>south of RTW Charleston</u> and <u>in front of the Library Society</u>.
- Videotaping and still photographing of work areas before, during and after completion of individual projects is an ongoing process. Site cleanliness and orderliness continues to be a priority. The "Pardon our Progress-Lower King is Open for Business" signs will be placed next week.
- As the sewer work progresses to reline the mains and lateral services to the buildings, it is probable that disruptions in water service for limited periods of time will occur. Streetscape staff will be in communication with merchants, residents and property owners in order to plan for this.

Most people are in favor of progress. It is the changes they don't like.

Author Unknown

Lower King Street Streetscape General / Preliminary Schedule

This preliminary schedule will change throughout the project. Depend on the weekly flyer for the most up-to-date and detailed information on Streetscape tasks, conditions and guidance.

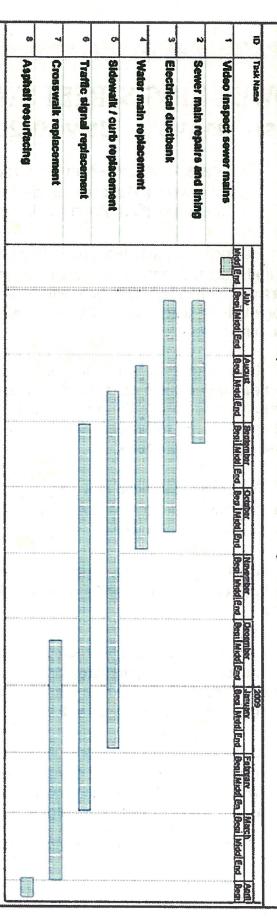

A schedule is a dynamic working tool!

Questions? Call Su 720-3886 or Brett 860-3696

	Propert Public Schedule Date Wed 7/2/109		
	Progress	9261	Task
	Project Summary	Summary	Miestono
Page 1	1	1	•
	Coadine	External Milestone	Extensel Tasks
	4	•	
	-		
	-		
